

# WCCUSD Bond Program Project Status Report



Citizen Bond Oversight Committee  
Measure M, D, J, D-2010 & E-2012

March 23, 2016






# ELEMENTARY SCHOOLS



# Nystrom Elementary School

Contract Value: \$21,188,102 Change Order: 3.44%

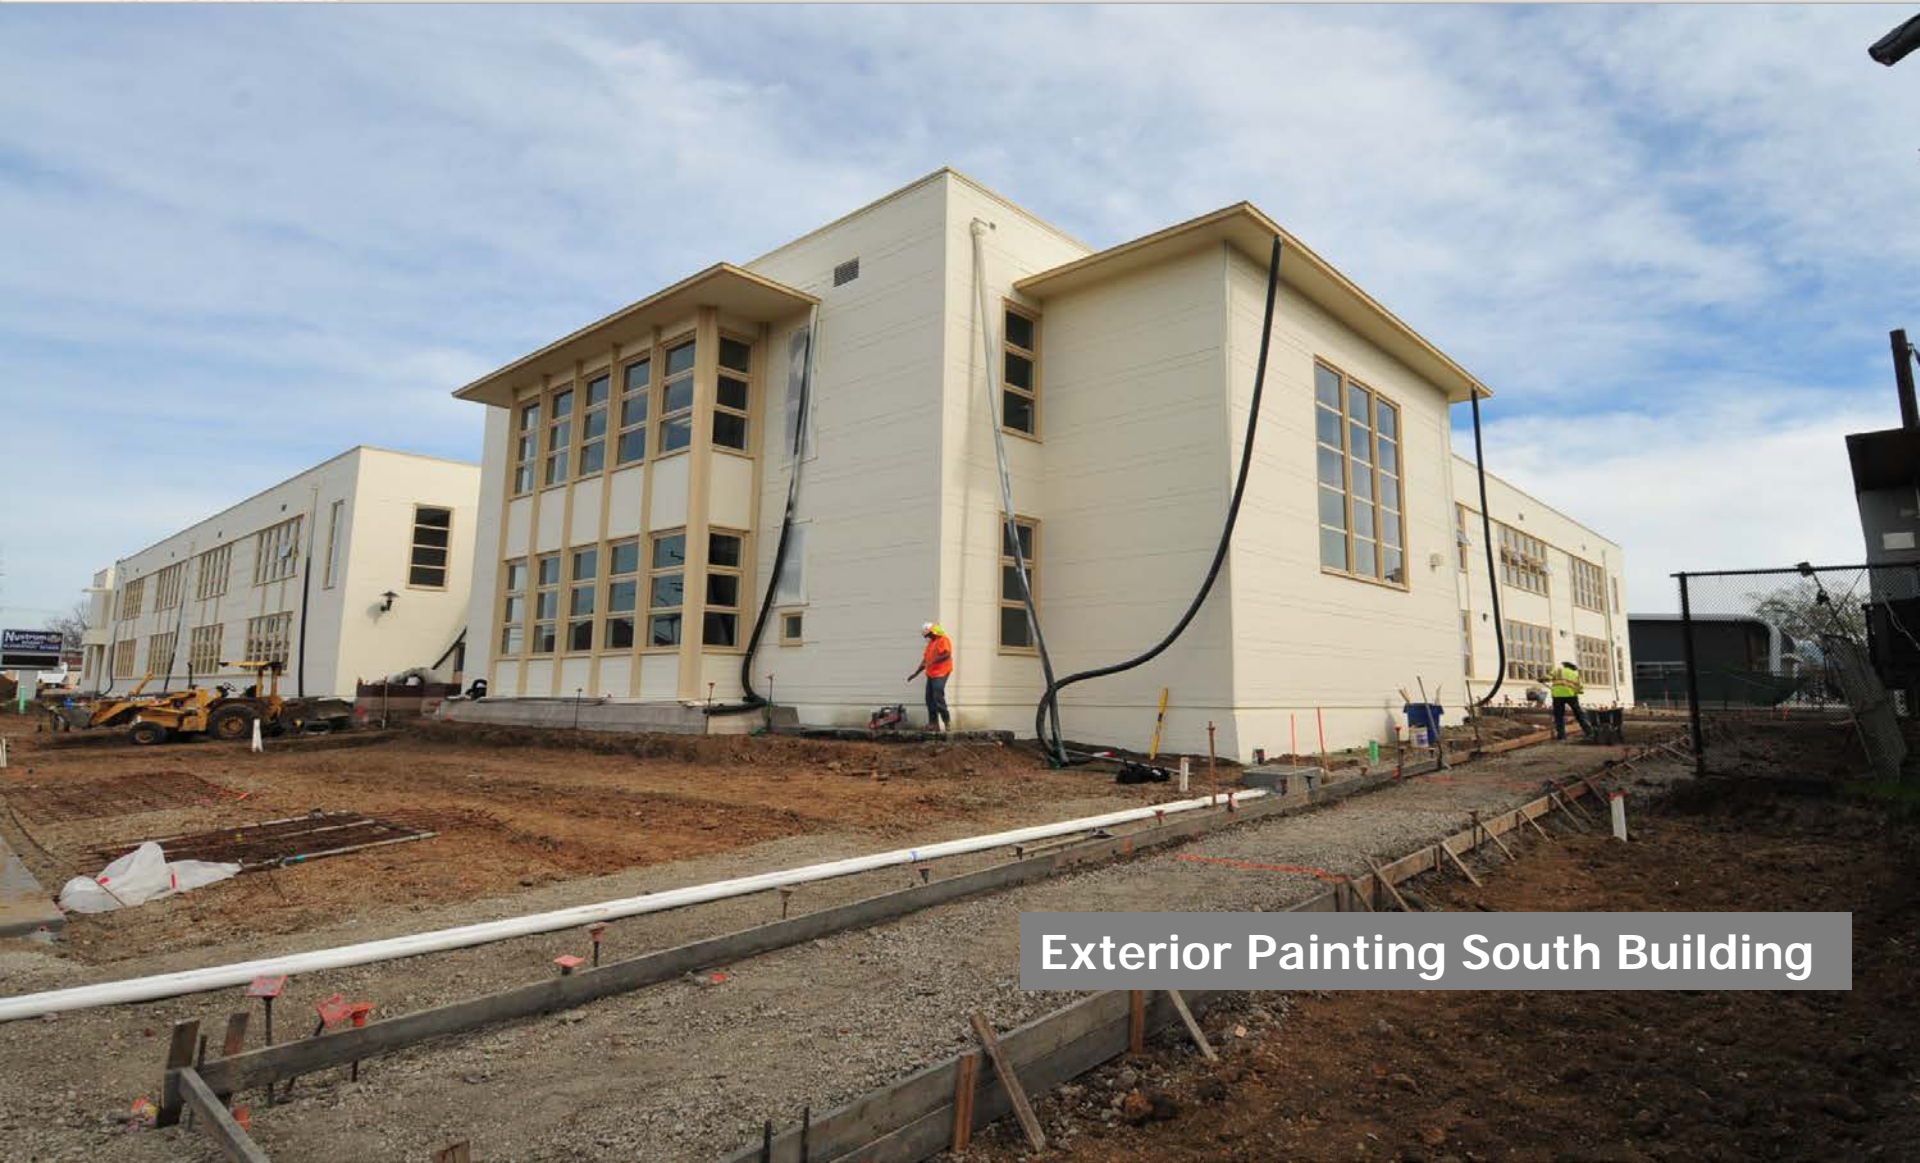

Exterior Painting South Building



Courtyard



South Building MP Connection



Corridor Hard Wood Floor



Typical Classroom Second Floor



# Valley View Elementary School Interim Campus

Contract Value: \$3,466,000    Change Order: 4.11%



Interim Office Building





# Lincoln Elementary School Building A Exterior Repairs

Contract Value: \$352,000



Exterior Painting



# MIDDLE SCHOOLS



# Fred T. Korematsu Middle School

Contract Value: \$42,762,406 Change Order: 3.13%



Level 1- Gate fence Installation



Level 1 - Basketball Courts



Level 2 - Site Concrete pour



Level 3 - Parking lot



7125

EASTRD  
SCHOOL

Site Landscaping



Building A - Teachers Lounge





Building B - Gymnasium



**Building C - Science Classroom**



**Building C - Dance Room**



# High Schools



# De Anza High School Linked Learning

Contract Value: \$17,750,953 Change Order: 3.17%



Building 10 Linked Learning



Sports Fields



# El Cerrito High School Stadium

Contract Value: \$13,438,000 Change Order: 6.68%



Site Overview



Concession & Courtyard



# Pinole Valley High School (PVHS) Project Status



Citizen Bond Oversight Committee Meeting  
March 30, 2016

# PVHS Anticipated Timeline

**Bids Received** - Apparent Lowest Responsible  
Responsive Bidder Identified 03/15/16

## **Next Steps:**

Receive CM Services Proposals 03/18/16

Bid Protest Period - 3 Business Days

5 Day Bid Withdrawal Period

Post-Bid Conferences 03/21/16 - 03/25/16

Special Facilities Subcommittee Meeting 04/04/16

BOE Bid Award (Target) 04/13/16

Notice to Proceed (Target) 05/02/16

Project Completion (Target) 11/02/18
