

WCCUSD Bond Program Project Status Report



Citizens' Bond Oversight Committee
Measure D-2002, J-2005, D-2010 & E-2012

February 24, 2016





ELEMENTARY SCHOOLS



Nystrom Elementary School

Contract Value: \$21,188,102 Change Order: 3.34%



Exterior Painting



Admin Building - Window Trim at Front Entrance



Typical Classroom Sanding
Hard Wood Floor



Typical Classroom Hard Wood Floor Finish



Valley View Elementary School Interim Campus

Contract Value: \$3,466,000 Change Order: 4.11%



Interim Office Building



New Playground Striping



Kindergarten Class



Dover Elementary School Synthetic Playfield

Contract Value: \$480,857

Change Order: 0.88%





Lincoln Elementary School Building A Exterior Repairs

Contract Value: \$352,000





MIDDLE SCHOOLS



Fred T. Korematsu Middle School

Contract Value: \$42,762,406 Change Order: 3.13%



Building C South Elevation
at Level 1




**Flat work outside Bldg. C at
site level 2 and Bldg. B
Library entrance**



Level 2 Rebar curb and flatwork



Building D East Elevation

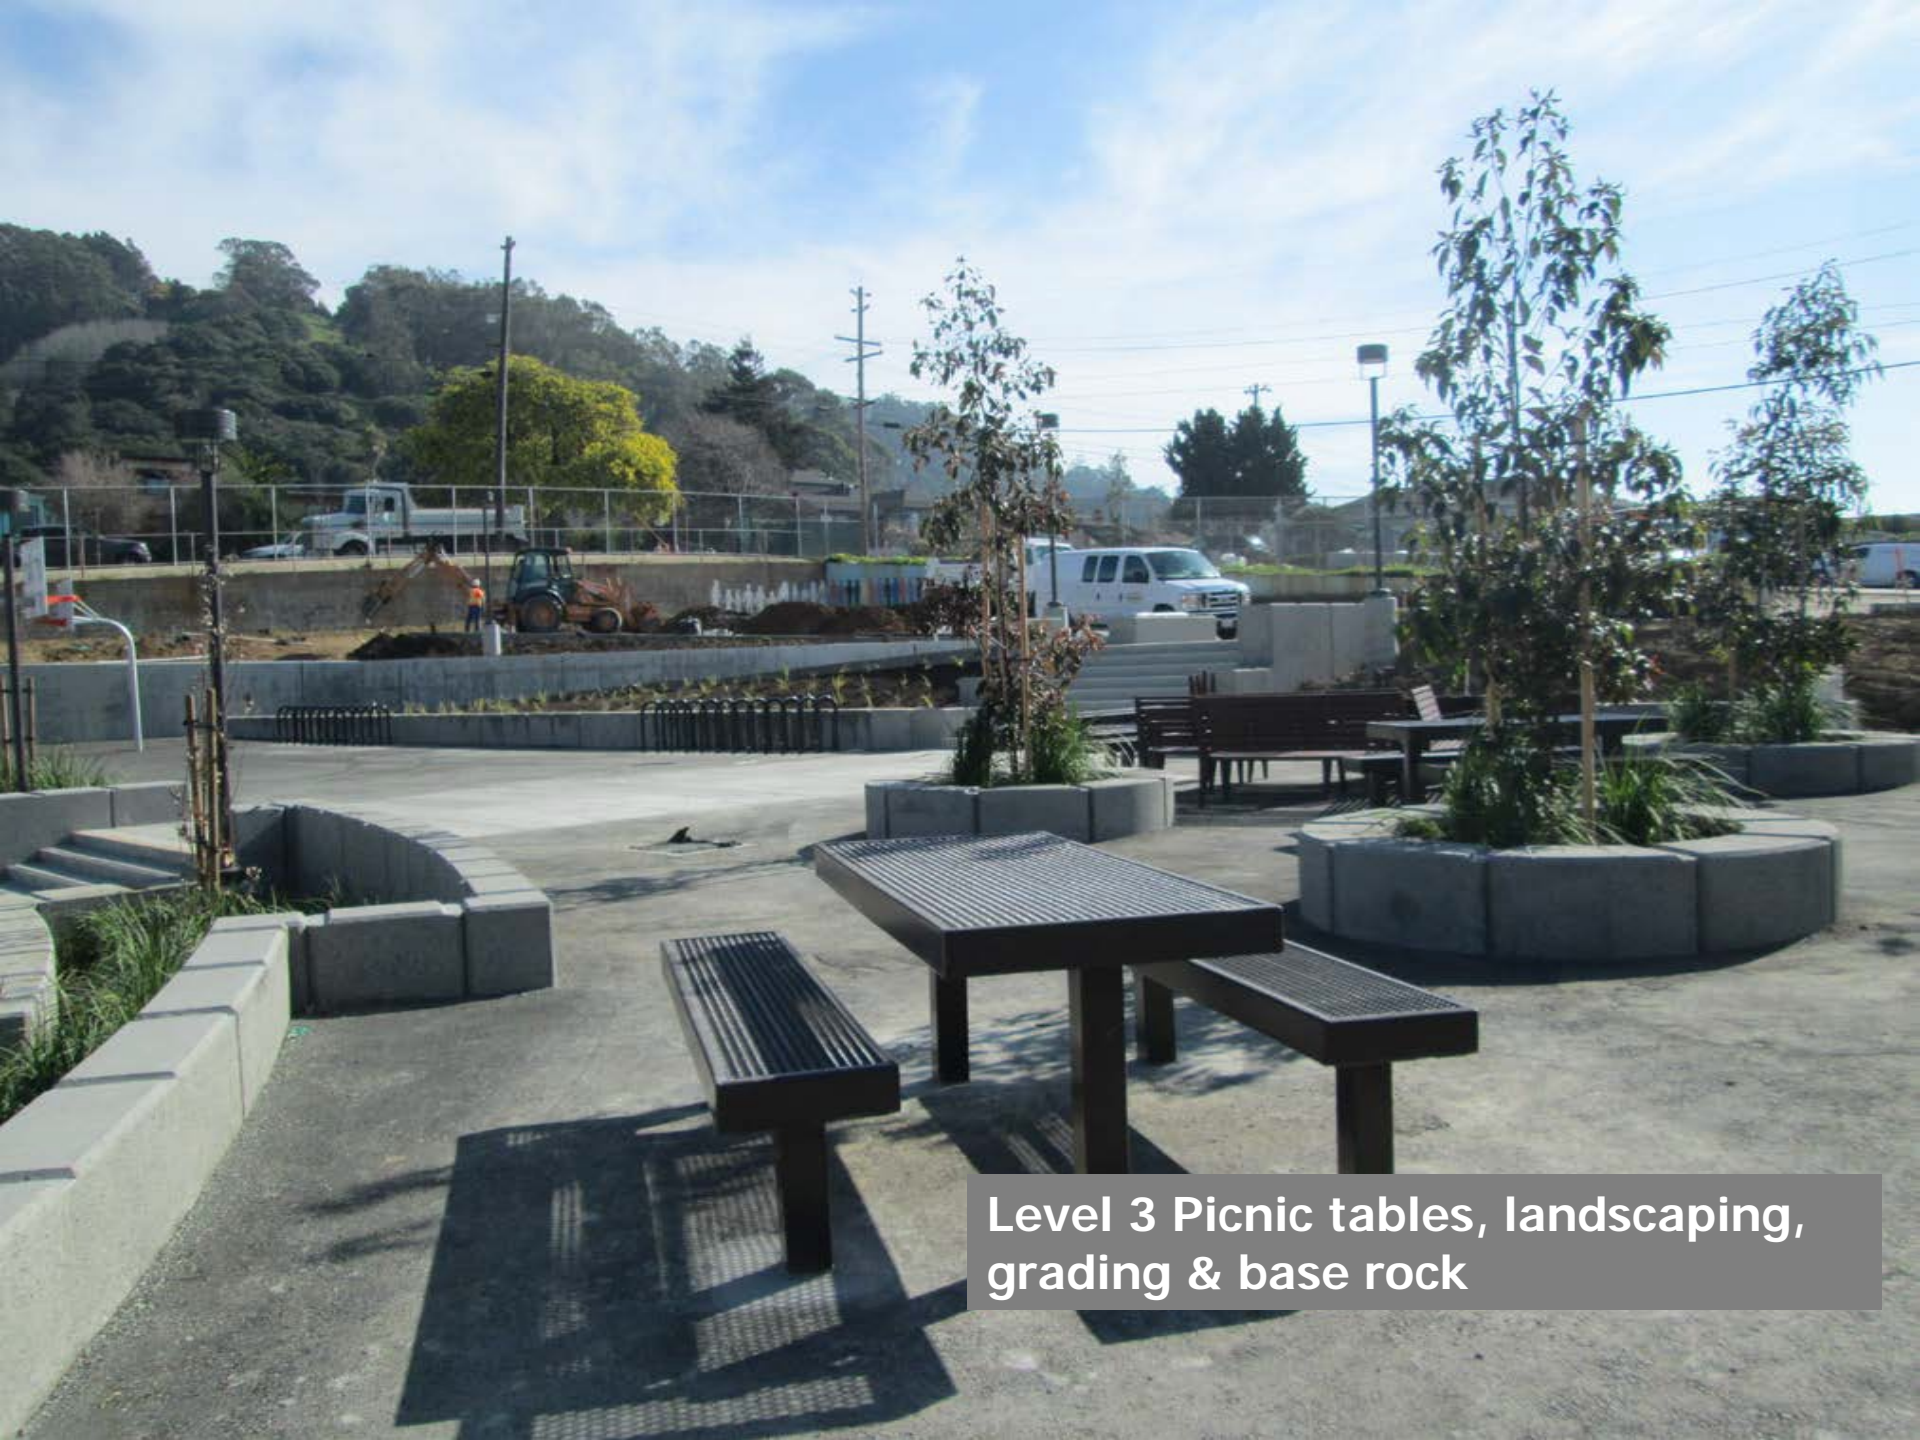

**Level 3 Picnic tables, landscaping,
grading & base rock**



Building A - Classroom
Furniture set up



Building B - Admin Lobby Area



**Building B - Gym Bleacher
Installation**



High Schools



De Anza High School Linked Learning

Contract Value: \$17,750,953 Change Order: 3.13%



Building 10 Linked Learning



HOME OF THE DONS
BALL STRIKE OUT
1 2 3 4 5 6 7 8 9

Softball Field



Soccer Field



Basketball Courts



Tennis Courts



El Cerrito High School Stadium

Contract Value: \$13,438,000 Change Order: 6.21%



Site Overview

EL CERRITO HIGH SCHOOL STADIUM
HOME OF THE GAUCHOS

Wall Lettering &
Landscaping



Colusa Slope



Weather Station

Pinole Valley High School (PVHS) Project Status



Citizen Bond Oversight Committee Meeting
February 24, 2016

PVHS Anticipated Timeline

Project Bid Period	Nov. 2015 – Mar. 2016
1 st Addendum	December 7, 2015
2 nd Addendum	December 23, 2015
3 rd Addendum	January 8, 2016
4 th Addendum	February 1, 2016
5 th Addendum	February 12, 2016
6 th Addendum (Scheduled)	February 19, 2016
7 th Addendum (Scheduled)	March 4, 2016
8 th Addendum (Scheduled)	March 10, 2016
Receive Blind Bids (Target)	March 15, 2016
BOE Bid Approval (Target)	April 13, 2016
