

WCCUSD Updating the 2016 Facilities Master Plan

July 2020



Hercules

Project Updates & Next Steps

Legacy Projects are bond - funded Projects that were in design or construction prior to the 2016 Facilities Master Plan

Legacy Project: PVHS Fields & Bleachers



Project Timeline:

Bleachers pending DSA Approval Bidding Process ~ 2 months Project Duration 18 months

PVHS BOE Approved Project Budget	\$216,549,580
Completed Projects	(\$197,365,450)
Remaining Project: Sports Fields/Bleachers	(\$19,184,130)

2016 Facilities Master Plan **Project Updates** & Next Steps

2016 Facilities Master Plan Project Status

Board Approved 2016 Facilities Master Plan Implementation Project Status								
School	Project Type	R.O.M. Cost (In Millions)	Total BOE Adjustments	Revised BOE Approved 02/26/20	Status			
Ed Specs &		0.2		0.2	Completed			
School Size Including All								
Sites in Master		TBD						
Cameron School	Critical Needs	1.3		1.30	Future Project			
Chavez ES	Critical Needs	0.6	-0.53	0.07	Completed			
Collins ES	Critical Needs	3.5		3.50	Future Project			
Crespi MS	Critical Needs	3.1	2.20	5.30	Construction			
Fairmont ES	Critical Needs	3		3.00	Construction			
Grant ES	Critical Needs	0.9	-0.69	0.211	Completed			
Harmon Knolls	Critical Needs	0.2	0.21	0.407	Completed			
Harmon Knolls	Soils Testing	0.1	-0.06	0.041	Completed			
Hercules HS	Critical Needs	7.2		7.20	Future Project			
Hercules MS	Critical Needs	7.5		7.50	Future Project			
Highland ES	Critical Needs	0.8		0.80	Design/Planning			
Kennedy HS	Critical Needs	12.2		12.20	Future Project			
Lake ES	RS Replacement	66.1	-1.50	64.60	Future Project			
Lake ES	RS Replacement		1.00	1.00	Design/Planning			
Lake ES	Critical Needs		0.15	0.148	Completed			
Ohlone ES	Critical Needs	0.8	-0.18	0.624	Completed			
Obama ES	RS Replacement	40.3		40.30	Construction			
Olinda ES	Critical Needs	1.0	-0.21	0.793	Completed			
Richmond HS	Critical Needs	15.1	5.9	21.00	Construction			
Riverside ES	Critical Needs	6.9		6.90	Design/Planning			
Shannon ES	Critical Needs	7.1		7.10	Future Project			
Stege ES	Critical Needs	2.9		2.90	Design/Planning			
Valley View ES	Critical Needs	1	0.09	1.091	Completed			
Total		181.8	6.389	188.189				

Projects in Construction or Closeout

- Michelle Obama Replacement Campus
- Richmond HS Critical Needs Project
- Fairmont ES Critical Needs Project
- Crespi MS Critical Needs Project (closeout)

Projects in Planning or Design

- Lake Replacement Campus
- Riverside ES Critical Needs Project
- Stege ES Critical Needs Project
- Highland ES

Projects to Commence FY 2021

- Kennedy HS Critical Needs Project
- Hercules MS/HS Critical Needs Project
- Shannon ES Critical Needs Project
- Collins ES Critical Needs Project
- Cameron Critical Needs Project

Michelle Obama School































Richmond High School Critical Needs

Seismic retrofit & ADA upgrades







Demolition of the old dance room & locker room which will soon be a new quad





New Gym, weight, dance, & locker room













Fairmont Elementary Critical Needs



n	
	F
*	
•	F

Fairmont Critical Needs Project
Parmont Education
Various classroom and
ADA improvements
As Life (A Seamoustan)
Confre Costs County S

Project Scope	Next Steps
Fairmont Site Expansion (non-bond)	
Demolish unoccupied senior center	Finalize Utility and connect
 Install new playground structure with safety mat 	to PG&E currently under
 Install 6 portables (providing space for special programs and additional restrooms) 	construction

Fairmont - FMP Critical Needs Project

- ADA stage lift
- Replace existing fire alarm (campus-wide)
- Add new staff and special education restrooms
- Classrooms Improvements
 - Plumbing repairs
 - Improve ADA accessibility in student restrooms
 - Replace existing classroom whiteboards
 - Paint classrooms & replace flooring

Remaining interior improvements currently under construction

Design Build Projects: Lake ES &

Riverside ES

Lake Elementary



Lake Elementary – Campus Replacement

FMP Scope of Work & Current Work

- Architect is developing bridging documents including phased construction options
- Stakeholder meetings are being conducted
- Survey and other site investigation being conducted

Remaining Budget: \$65.6M

Next Steps

- BOE Approval of Remaining Project Budget Allocation
- 2. Complete the RFQ/RFP process for a design build team **Fall 2020**
- Design Build Entity's execution of design and construction –
 Construction timeline will be dependent on phasing

Riverside Elementary




Riverside Elementary – Critical Needs Project

- FMP scope included resolving soil stabilization by relocating the multipurpose room and some of the classroom buildings
- Staff is pursuing a soil stabilization scope which will create stable soil and mitigate the need to relocate buildings

Budget \$6.9M

- Complete the RFQ/RFP process for a design build team
- Design Build Entity's approval and execution of stabilization measures and completion of the project

Scope of Work Confirmation






FMP Scope of Work	Next Steps
Stege Elementary – Critical Needs Project	
 Master plan scope included moving school functions to existing portables and demolish Building 1 	Confirm program requirements and finalize scope
Creating a new drop off and portable office location	'
Interior improvements to the existing building	
Budget: \$2.9M	
Highland Elementary – Critical Needs Project	
 FMP scope of work was completed in 2018 for a total cost of \$53K. Remaining Project budget to replace water main and update PG&E transformer to extend the useful life of facility 	Confirm power and water needs and finalize scope
Remaining Budget: \$747,125	

Next Phase of 2016 Master Plan Projects

building shared by Hercules Middle and High

Hercules Middle School Budget: \$7.5M Hercules High School Budget: \$7.2M

School





FMP Scope of Work Next Steps Kennedy High - Critical Needs Project Master plan scope includes demolishing the front 1. Confirm program building, reorienting the campus and using the requirements and define portables on site as a temporary campus until a scope larger rebuild could occur 2. Request Board approval of Budget: \$12.2M project budget **Hercules Middle & High - Critical Needs Project** 1. Confirm program requirements and define Replace portables and build modern science

scope

2. Request Board approval of

project budget

Next Phase of 2016 Master Plan Projects








FMP Recommendations	Next Steps
 Shannon Elementary - Critical Needs Project Replace multipurpose room in a new location. Budget: \$7.1M 	 Confirm program requirements and define scope Request Board approval of project budget
 Collins Elementary - Critical Needs Project Install new heating, ventilation, and air conditioning to replace boiler system Remove or repair stage in Multipurpose Room Budget: \$3.5M 	 Investigate and select best option for HVAC system replacement Request Board approval of project budget
• Critical Needs Project • Critical Needs: ~\$1M for various critical needs Budget: \$1.3M	 Prioritize facilities needs and define scope Request Board approval of project budget

Site Budget Authorization

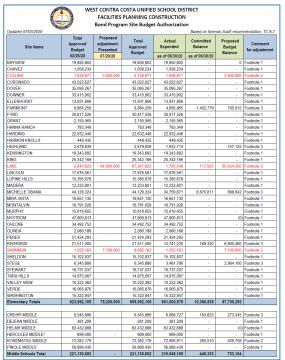

Site Name	Total Approved Budget	Proposed adjustment Presented	Total Approved Budget	Actual Expended	Committed Balance	Proposed Budget Balance	Comment for adjustmen
	02/26/20	07/29/20		as of 06/30/20	as of 06/30/20		
DE ANZA HIGH	132 236 248		132 236 248	132 236 248			Footnote 1
EL CERRITO HIGH	146,850,105		146,850,105	146,850,105		- (0)	Footnote 1
GREENWOOD ACADEMY/LPS	79.583.607		79.583.607	79.583.607			Footnote 1
HERCULES HIGH*	3 295 019	14 700 000	17 995 019	3 295 019	- :	14 700 000	
KENNEDY HIGH	33.854.981	12,200,000	46.054.981	33.854.981	-	12,200,000	
PINOLE VALLEY HIGH	216.549.580	12,200,000	216.549.580	196,269,051	867.334	19,413,194	
RICHMOND HIGH	42 622 087		42.622.087	29 540 849	12 777 102		Footnote 3
VISTA HIGH	7 236 543		7.236.543	7 236 543	12,111,102		Footnote 1
High Schools Total	662.228.170	26.900.000	689.128.170	628.866.403	13.644.436	46.617.331	FOORIOUS I
nigii aciioois Total	002,220,170	20,500,000	003,120,170	620,000,403	13,044,430	40,017,331	
ADAMS MIDDLE	691.211		691,211	691.211			Footnote 1
CAMERON	122 195	1,300,000	1 422 195	122 195	-	1 200 000	Footnote 3
CASTRO	620,944	1,000,000	620 944	620 944	- :	1,000,000	Footnote 1
DELTA NSS DEANZA	152 226		152 226	152 226	- :		Footnote 1
EL SOBRANTE	536 231		536 231	536 231	- :	-	Footnote 1
HARBOUR WAY COM DAY	121.944		121.944	121.944			Footnote 1
KAPPA NSS KENNEDY	109.831		109.831	109 831			Footnote 1
NORTH CAMPUS	205.450		205.450	205.450		-	Footnote 1
OMEGA NSS RICHMOND	118 313		118.313	118 313			Footnote 1
SEAVIEW	499 116		499 116	499 116			Footnote 1
SIGMA NSS PVHS	110.949		110.949	110.949			Footnote 1
TRANS LEARNING CENTER	116.673		116.673	116.673			Footpote 1
WEST HERCULES FLEM	56.847		56.847	56.847			Footnote 1
Closed Schools/Programs Tot	3.461.930	1.300.000	4.761.930	3.461.930		1.300.000	
	0,101,100	1,000,000	4,101,000	4,101,100		1,000,000	
CENTRAL	102.831.634		102.831.634	98.069.563	1.031.377	3 730 694	Budget thru 20-2
RCP CHARTER	4 415 204		4.415.204	4 415 204	.,,	-,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	Footpote 1
INFORMATION TECHNOLOGY	35.000.000		35.000.000	34.294.330		705.670	Footnote 2
Admin/Other Total	142,246,838		142,246,838	136,779,097	1,031,377	4,436,364	
	,,		,,	,,	.,,,,,,,,,	4,004,000	
GRAND TOTAL	1,652,929,646	103,400,000	1.756.329.646	1.590.056.574	25.485.982	140,787,090	

ıs	Lake ES Campus Replacement Budget
	Kennedy HS Critical Needs Project
	Cameron Critical Needs Project
	Hercules MS/HS Critical Needs Project
	Collins ES Critical Needs Project
	Shannon ES Critical Needs Project

Financial Impact

Projects

Budget

Allocations

Bond Program Financial Status June 30, 2020 Preliminary	Current	Estimated
Projected Cash Balance at June 2021	103,596,266	196,266
Total Bond Program Budget	1,652,929,646	1,756,329,646
2016 Facilities Master Plan Budget	188,188,828	188,188,828

Review of the 2016 Facilities Master Plan

Process & Progression

Long Range Facilities Master Plan

Approved by the Board of Education on 6/15/16

"Our Children, Our Schools, Our Future"

Available Online https://www.wccusd.net/Page/6945

Stewarding Bond Funds

The Facilities Master Plan was created in **active consultation with the community** and sets a course of action adaptable over time since many variables are unknown or beyond our control.

WCCUSD Master Plan End Goals



Identify the order in which projects on the Priority Sites would be completed based on equitable, measureable criteria.

Define construction projects with budgets


Establish the Implementation Plan that prioritizes a clear course of action to address facilities needs







2016 Facilities Master Plan Process & Progression

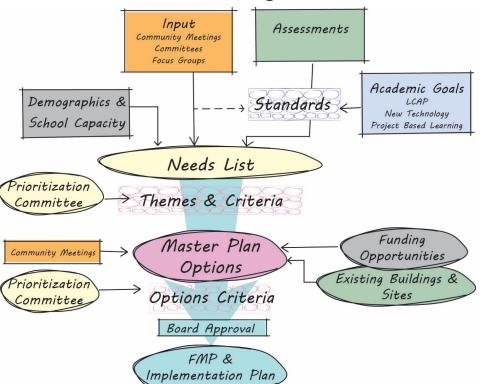







2016 Facilities Master Plan Process & Progression



Prioritization Committee Purpose & Membership

A Prioritization Committee ("Committee") with 15 members was formed to consider and recommend criteria for project sequencing to the Board.

Elementary Parent Kennedy HS Family	Elementary Parent Richmond HS Family	Elementary Parent El Cerrito HS Family	Elementary Parent De Anza HS Family	Elementary Parent Pinole HS Family
Elementary Parent Hercules HS Family	City of Richmond	City of El Cerrito	City of San Pablo	City of Hercules
City of Pinole	County	K-12 Operations	K-12 Operations	K-12 Operations

2016 Facilities Master Plan Process & Progression

Criteria Input
Community Meetings
Site Meetings
Board
CBOC

Prioritization Committee

Board Approval of Prioritization Criteria

Apply Criteria to the 21 Priority Sites to determine Sequencing

2016 Prioritization Criteria

- Committee considered 25 criteria generated at site & community meetings
- Committee added, split, combined and narrowed the criteria into final

Years since last improvement

Site Functionality

Seismic Needs

Age of School

Physical Condition

ADA Compliance Completed Phases of Design Economically Disadvantaged Area

Eligible for State Funding

% of Enrollment ESL, Foster or Low Income Lack of Technology Infrastructure

Over or Nearing Capacity

Updating the 2016 Facilities Master Plan

Incorporating Measure R

Measure R Ballot Language

21 Priority School Projects



Campus Replacement part of 2016
Implementation Plan

Wilson Elementary School

Lake Elementary School


Types of Projects

Priority School Sites:
Construction,
Renovation, Repair &
Upgrade Projects

District-Wide School Health, Safety and Security, Earthquake Safety & Energy Efficiency School Projects

District-Wide Wiring & Instructional Technology Projects for Effective Learning Environment and Job Training

Master Plan Update – Incorporating Measure R

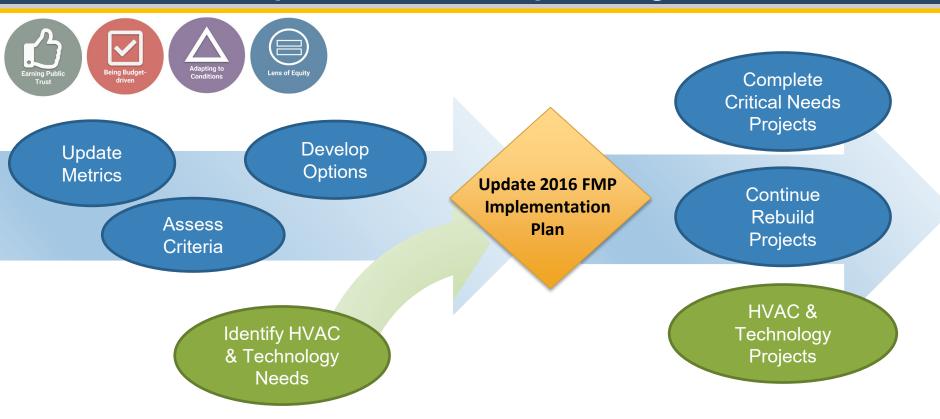

2020
Prioritization
Committee
Role &
Responsibilities

- Use community input to discuss existing criteria and any additional criteria to be considered
- Recommend how to update the criteria
- Which existing criterion is no longer applicable
- Which criterion and associated metrics should be added
- How to weight each criterion

Reforming the Prioritization Committee

The Committee would evaluate and recommend to the Board which metrics should be updated and the weight of each criteria

Parent Richmond HS Family	Parent Kennedy HS Family	Parent El Cerrito HS Family	Parent De Anza HS Family	Parent Pinole HS Family	Parent Hercules HS Family
Student Representative Richmond HS Family	Student Representative Kennedy HS Family	Student Representative El Cerrito HS Family	Student Representative De Anza HS Family	Student Representative Pinole HS Family	Student Representative Hercules HS Family
Representative Business & Operations	Representative from Special Education	Representative from Academics	MDAC Representative	DLCAP Representative	AASAT Representative

Updating our Metrics to Reflect 2020 Data

Seismic Needs

Structural reports prepared for the District in 2002

Completed Phases of Design

 No Design, Master Plan, Schematic Design, Design Development, Construction Drawings, DSA set

Economically Disadvantaged Area

Median Income of the Census Track

Eligible for State Funding

Eligibility for state funding

% of Enrollment ESL, Foster or Low Income

LCAP unduplicated count

Lack of Technology Infrastructure

Assessment scores prepared by Technology department

Over or Nearing Capacity

Utilization using capacity without portables


2020 Facilities Master Plan Next Steps



Assessing Prioritization and Incorporating Measure R Next Steps

- Reforming the Prioritization Committee & Issuing Community Survey
- Present the Criteria to the Board
- 3. Present the Updated List of Priority School Sites based on approved Criteria
- 4. Refine Project scopes for Priority Schools, HVAC & Tech
- 5. Present Options to the Board
- 6. Present Implementation Plan to Board (scope, sequence, budget)

2020 Facilities Master Plan Next Steps



Assessing Prioritization and Incorporating Measure R Timeline

Summer / Fall 2020:

Reform the Prioritization Committee

Issue Community Survey

Update Metrics to 2020 data HVAC Study

Present the Criteria to the Board

Present the Updated List of Priority School Sites based on the Board approved Criteria

Winter 2020:

Refine Project scopes for Priority Schools, HVAC & Tech

Present Options to the Board

Spring 2021:

Present Implementation Plan to Board (Scope, Schedule & Budget)
